Public - عام

Kingdom of Saudi Arabia
Ministry of Education
Imam Abdulrahman bin Faisal University
College of Science and Humanities-Jubail
Computer science Department

Software Engineering
Term 1 – 2026/2027

Software Project Management Plans

For

Food Saver

Version 1.0

Name of Team: CS Year 5, SE Old Section, G1

Project Advisor: Dr. Enas El-Sayed Mohammed El-Sharawy

17 October 2026

This Software Project Management Plan (SPMP) was prepared and provided as a deliverable for Software Engineering Course (CS 411), Term 1 – 2026/2027, and it will be used by the Food Saver team and our course instructor to plan and follow up the project.

This document is based in part on the IEEE Recommended Practice for SPMP Descriptions.

Team Members

#	Name	ID	Role	Signature
1	Aljazi Alsaiari	2230004865	Leader	
2	Roweena Belal	2230005940	Member	
3	Noor Alawami	2230000703	Member	
4	Forat Alabbas	2230001270	Member	

Sections written by each member:

#	Name	Documentation Section
1	Aljazi Alsaiari	Section 1: Project Overview
2	Noor Alawami	Section 2: Project Organization, Section 5: Supporting Process Plans
3	Roweena Belal	Section 3: Managerial Process Plans
4	Forat Alabbas	Section 4: Technical Process Plans, Section 6: Additional Plans

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Table of Content

Revision History....4
Table of Tables....5
Table of Figures....6
1. Project Overview....7
1.1 Purpose, Scope, and Objectives....7
1.2 Assumptions, Constraints, and Risks....8
1.3 Project Deliverables....9
1.4 Schedule and Budget Summary....10
1.5 Evolution of the Plan....10
1.6 References....10
1.7 Definitions and Acronyms....11
1.8 Document Structure....12
2. Project Organization....13
2.1 External Interfaces....13
2.2 Internal Structure....13
2.3 Roles and Responsibilities....14
3. Managerial Process Plans....16
3.1 Start-up Plan....16
3.1.1 Estimates....16
3.1.2 Staffing....16
3.1.3 Project Staff Training....16
3.2 Work Plan....16
3.2.1 Work Breakdown Structure....16
3.2.2 Schedule Allocation....17
3.2.3 Resource Allocation....19
3.2.4 Budget Allocation....19
3.3 Project Tracking Plan....19
3.3.1 Requirements Management....19
3.3.2 Schedule Control....19
3.3.4 Quality Control....20
3.3.5 Reporting....20
3.3.6 Project Metrics....20
3.4 Risk Management Plan....20
3.5 Project Closeout Plan....21
4. Technical Process Plans....22
4.1 Process Model....22
4.2 Methods, Tools, and Techniques....23
4.3 Infrastructure....23

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

4.4 Product Acceptance..... 23
5. Supporting Process Plans..... 24
5.1 Documentation..... 24
6. Additional Plans..... 25

Revision History

Name	Date	Reason For Changes	Version
Aljazi Alsaiari	Oct 17, 2026	Prepared initial version	1.0

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Table of Tables

Table 1: Definitions and acronyms 11
Table 2: Project tasks, durations and dependencies 17
Table 3: Project milestones 18
Table 4: Project metrics 20
Table 5: Risk identification 20
Table 6: Risk analysis 21
Table 7: Risk planning 21
Table 8: Details about project documents 24

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Table of Figures

Figure 1: External interface 13
Figure 2: Internal structure 14
Figure 3: Organizational structure 14
Figure 4: Roles and responsibilities 15
Figure 5: Work breakdown structure 17
Figure 6: Activity bar chart 18
Figure 7: Staff allocation chart 19
Figure 8: Scrum process model of the project 23

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

1. Project Overview

1.1 Purpose, Scope, and Objectives

1.1.1 Background and Purpose

Food waste is a big problem in many homes. People buy food and then forget about it, or they do not notice the expiry date until it is too late. Around the world, households alone waste about 79 kg of food per person every year [1]. Research shows that household food waste is linked to daily habits like planning, shopping, storing food, and understanding expiry dates [2], [3]. Food waste is also a serious problem in Saudi Arabia, and it affects both the economy and the environment [4].

Mobile applications can help people manage their food better. Studies found that apps that track food and send reminders can help households reduce their food waste [5], [6].

At the same time, there are families in the same neighborhood who need food. Food sharing apps showed that connecting neighbors can help redistribute extra food instead of throwing it away [7]. However, there is still no simple local app that joins food tracking and food donation together.

Food Saver is a mobile application prototype that helps with both problems. It helps users track the food they have and its expiry dates, reminds them before food expires, suggests recipes using what they already have, and lets them donate extra food to people nearby.

The purpose of this Software Project Management Plan (SPMP) is to explain how our team will plan and manage the Food Saver project. It covers the scope, objectives, schedule, resources, risks, and the way we will work. This plan follows the IEEE 1058 standard. The project will not be implemented. It will focus on documentation (planning, requirements, design, and testing) and a high-fidelity prototype made in Figma.

1.1.2 Scope

The scope of Food Saver is to create complete documentation and an interactive prototype for a food management and donation app.

The main modules of the Food Saver prototype are:

1. **Food Inventory:** users add the food items they have with the quantity and expiry date.
2. **Expiry Alerts:** the app sends reminders when an item is close to its expiry date.
3. **Smart Recipe Suggestions:** the app suggests recipes based on the items the user has, and gives priority to items that will expire soon.
4. **Food Donation:** users can post extra food for donation or request food they need.
5. **Search and Filter:** users can search donations by food category, donation type, location, and quantity.
6. **Donation Matching:** the app matches donations with nearby requests based on location, food type, and quantity.
7. **Recipe Community:** users can share, discover and rate recipes.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

8. **Rewards:** users get points for completed donations, and these donations are counted as volunteer hours through a volunteering platform.

In this first version, we will focus on these eight modules only. Bigger extensions are not included, like food delivery or linking the app with supermarkets. There is also no coding or real database, so things like location matching, alerts, and the link with the volunteering platform are shown in the prototype using sample data. Our documents will include the main design diagrams and a risk analysis. We will also keep the design divided into separate modules, so new features can be added easily in the future.

1.1.3 Objectives

- Design an easy and user-friendly prototype that helps households reduce food waste.
- Help users keep track of their food and expiry dates in one place.
- Remind users before their food expires.
- Suggest recipes that use the items that will expire first.
- Make it easy to donate extra food and to find food donations nearby.
- Encourage users to keep using the app through the recipe community and rewards.
- Produce complete project documents that follow IEEE standards.

1.1.4 Success Metrics

The project will be considered successful if:

- Users can move around the prototype easily without getting lost.
- Users can add a food item and create a donation without help during testing.
- Test users are satisfied with the recipe suggestions and the community screens.

We will check these through scenario-based usability tests, where classmates and family members try to finish real tasks in the prototype, like adding a food item or posting a donation. We will also review the screens using Nielsen's usability heuristics [8]. After each sprint, we will use the instructor feedback, and later the test results, to improve the design. This helps us find problems early and keep the risks under control.

1.1.5 Relationship to Other Projects

Food Saver is a new project, and it is not part of any other project. In the future, the app can be fully developed and published as a real mobile application. It can also be connected with real systems, such as the national volunteering platform and local food charities, so donations and volunteer hours are recorded officially.

1.2 Assumptions, Constraints, and Risks

1.2.1 Assumptions

- The course instructor will give feedback on each document on time.
- Each team member will work about 8 hours per week on the project.
- Classmates and family members will help us test the prototype and give honest feedback.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

- Free tools such as Figma, Zoom and WhatsApp will stay available for us.

1.2.2 Constraints

- **Time Constraint:** we only have one semester (15 weeks) to finish all the documents and the prototype, while we also study other courses.
- **Budget Constraint:** there is no budget, so we only use free tools and our own devices.
- **Quality Constraint:** all documents must follow the course templates and the IEEE standards, such as IEEE 1058 for the SPMP [9] and IEEE 829 for the test plan [10].
- **Scope Constraint:** only a prototype will be delivered. There is no coding or real launch of the app.
- **Technology Constraint:** the prototype cannot show real alerts or real location matching, so we use sample data.

1.2.3 Risk Assessment

We will keep checking risks during the whole semester, not only at the start. The main risks we expect are:

- **Schedule Risks:** Other courses and exams may delay our work. We will plan early and set our own deadlines before the real ones.
- **Scope Risks:** the app has many features for one semester. We will focus on the main features first.
- **Human Risks:** a member may be absent or busy. Each member will know the work of the others so anyone can continue.
- **Technical Risks**: the prototype cannot show real features like alerts or location matching, since there is no code. We will use sample data and clear screen flows in Figma to show how these features work.
- **External Risks:** Online tools like Figma, Google Drive, or Blackboard may stop working for a short time, or the internet may go down close to a deadline. To reduce this, we will keep local copies of our files on our laptops, back up our work on Google Drive, and try to submit a day before the deadline.

More details about the risks are in section 3.4.

1.3 Project Deliverables

Food Saver has eight main milestones during the semester. M1 is the project proposal, which was approved in Week 4. M2 is the SPMP. It covers the project goals, scope, risks, and management plan. M3 is the first Status Report, which shows the progress made so far.

M4 is the SRS. It includes the functional and non-functional requirements of Food Saver based on user needs. M5 is the SDS, which includes the system design, diagrams, and main screens.

M6 is the second Status Report. M7 is the STP, which explains the test cases, expected results, and how the prototype will be tested. M8 is the final Figma prototype and the final presentation of the project.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Before submitting each document, the team checks the work to make sure it is complete and follows the course requirements. All project files are submitted through Blackboard.

1.4 Schedule and Budget Summary

1.4.1 Schedule

Food Saver follows Agile planning using Scrum [11], [12], as stated in our proposal. As our course book explains, the project goes through three phases [11]: a first planning phase, a number of sprints, and a closing phase. At the start of the semester, we made a release plan that shows all the deliverables and their deadlines. Then, at the start of each sprint, we do iteration planning, where we choose the tasks of that sprint and divide them between the members [11]. Each sprint is two weeks long:

- Initial phase (Weeks 1-7): choosing the idea, writing the project proposal and the SPMP.
- Sprint 1 (Weeks 8-9): first status report, collecting the requirements, and starting to update the prototype.
- Sprint 2 (Weeks 10-11): writing the SRS and the SDS, and finishing the prototype update.
- Sprint 3 (Weeks 12-13): second status report, testing the prototype with users, and writing the STP.
- Closure phase (Weeks 14-15): improving the prototype, the final presentation, and what we learned from the project.

At the end of each sprint, the team reviews the work and uses the feedback from the instructor or the team to improve the next one.

1.4.2 Budget

There is no need for a formal budget because the team uses free software and personal devices. The estimated work effort is 4 team members × 8 hours per week × 15 weeks, which gives about 480 person-hours.

Some small personal expenses, such as printing and internet access, may cost around 150 SAR per member, or about 600 SAR for the whole team. These are personal expenses paid by the members, not a formal project budget.

1.5 Evolution of the Plan

This SPMP is a living document, which means it can change during the project. We will update it after each main milestone or if we find new risks or changes. Any update will be discussed with the team first and shared with the instructor if needed.

All versions of the document are saved in a shared Google Drive folder, and each new version gets a new number in the Revision History table.

1.6 References

[1] United Nations Environment Programme, “Food Waste Index Report 2024,” UNEP, Nairobi, 2024.

[2] D. Quested, E. Marsh, D. Stunell, and A. Parry, “Spaghetti soup: The complex world of food waste behaviours,” Resources, Conservation and Recycling, vol. 79, pp. 43–51, 2013.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

[3] M. Hebrok and C. Boks, “Household food waste: Drivers and potential intervention points for design – An extensive review,” J. Cleaner Production, vol. 151, pp. 380–392, 2017.

[4] M. B. Baig et al., “Food waste in Saudi Arabia: Causes, consequences, and combating measures,” Sustainability, vol. 14, no. 16, p. 10362, 2022.

[5] C. Castro et al., “Less is more: Preventing household food waste through an integrated mobile application,” Sustainability, vol. 15, no. 13, p. 10597, 2023.

[6] G. Mastorakis et al., “Managing household food waste with the FoodSaveShare mobile application,” Sustainability, vol. 16, no. 7, p. 2800, 2024.

[7] J. Harvey, A. Smith, J. Goulding, and I. Branco Illodo, “Food sharing, redistribution, and waste reduction via mobile applications: A social network analysis,” Industrial Marketing Management, vol. 88, pp. 437–448, 2020.

[8] J. Nielsen, “Enhancing the explanatory power of usability heuristics,” in Proc. SIGCHI Conf. Human Factors in Computing Systems (CHI ’94), Boston, MA, USA, 1994, pp. 152–158.

[9] IEEE Std 1058-1998, “IEEE Standard for Software Project Management Plans,” IEEE, 1998.

[10] IEEE Std 829-2008, “IEEE Standard for Software and System Test Documentation,” IEEE, 2008.

[11] I. Sommerville, Software Engineering, 10th ed. Boston, MA, USA: Pearson, 2016.

[12] K. Schwaber and J. Sutherland, “The Scrum Guide,” Nov. 2020. [Online]. Available: https://scrumguides.org

[13] IEEE Std 830-1998, “IEEE Recommended Practice for Software Requirements Specifications,” IEEE, 1998.

[14] IEEE Std 1016-2009, “IEEE Standard for Information Technology—Systems Design—Software Design Descriptions,” IEEE, 2009.

1.7 Definitions and Acronyms

Table 1: Definitions and acronyms

Acronym / Term	Definition
SPMP	Software Project Management Plan: explains how the project will be planned and managed.
SRS	Software Requirements Specification: describes what the system should do.
SDS	Software Design Specification: describes how the system is designed.
STP	Software Test Plan: describes how the system will be tested.
Sprint	A short work period in Scrum that ends with a finished part of the work.
Prototype	A clickable model of the app made in Figma, without code.
UI/UX	User Interface and User Experience.
WBS	Work Breakdown Structure: divides the project into smaller tasks.
UML	Unified Modeling Language: used to draw system diagrams.
Scrum	An Agile method where work is done in short cycles called sprints.
IEEE	Institute of Electrical and Electronics Engineers.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Acronym / Term	Definition
IAU	Imam Abdulrahman Bin Faisal University.

1.8 Document Structure

This SPMP includes the Revision History, Table of Tables, and Table of Figures, followed by:

- **Section 1 – Project Overview:** purpose, scope, objectives, assumptions, constraints, risks, deliverables, schedule, and budget.
- **Section 2 – Project Organization:** external interfaces, internal structure, and roles and responsibilities.
- **Section 3 – Managerial Process Plans:** start-up plan, work plan, tracking plan, risk management, and closeout.
- **Section 4 – Technical Process Plans:** process model, tools, infrastructure, and product acceptance.
- **Section 5 – Supporting Process Plans:** documentation.
- **Section 6 – Additional Plans:** other plans for the project.

This structure follows the course template and the IEEE SPMP standard.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

2. Project Organization

2.1 External Interfaces

Dr. Enas El-Sharawy is the project supervisor. The supervisor is the main link between the project team and the external entities, as shown in Figure 1.

The supervisor follows our progress in all phases, gives us advice and feedback, and makes sure the work meets the course requirements. The parent organization is Imam Abdulrahman Bin Faisal University, Computer Science Department. The external entities are the end users of the app, such as households, food donors, people who need food, and home cooks, who will help us test the prototype.




Figure 1: External interface

2.2 Internal Structure

The team is led by the project leader, who divides the tasks, follows the progress, and makes sure the work is done on time. The project leader also works as the design manager and is responsible for designing the prototype. The team also includes a planning manager who is responsible for the schedule and meetings, a technical writer who prepares and formats the documents, and a test manager who checks the quality and prepares the test plan.

The team communicates through face-to-face meetings at the university, Zoom meetings, and a WhatsApp group for quick updates.

Figure 2 shows the internal structure, and Figure 3 shows the organizational structure of the team. Each member reports to the project leader, and the project leader communicates with the supervisor.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

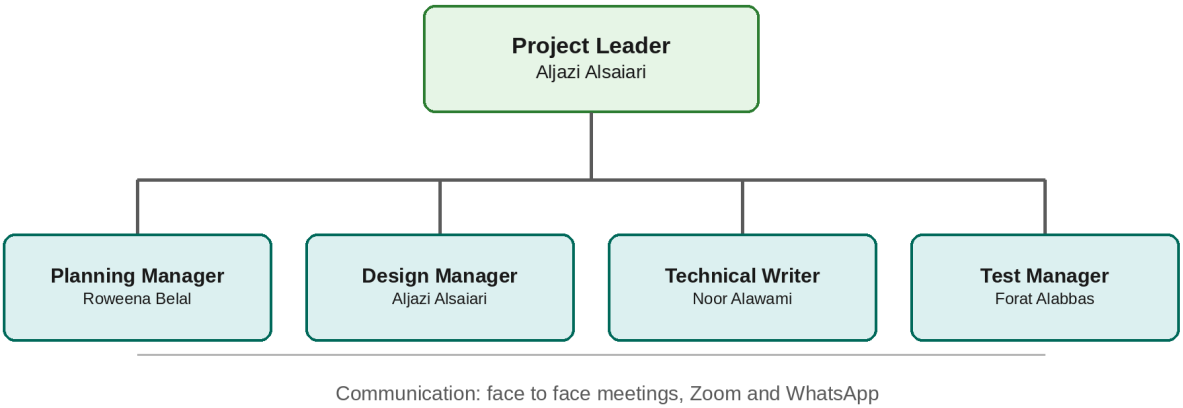


Figure 2: Internal structure

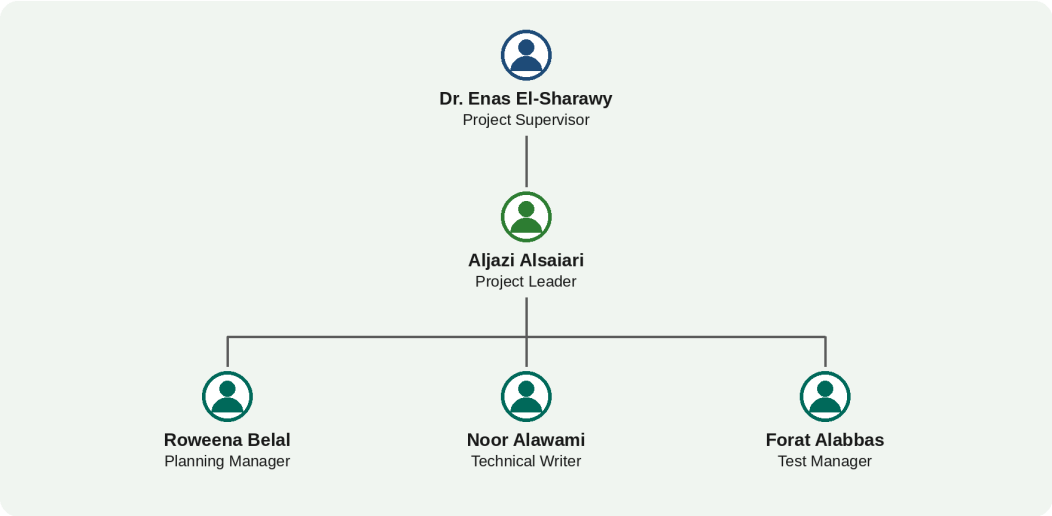


Figure 3: Organizational structure

2.3 Roles and Responsibilities

Giving each member a clear role helps us organize the work and divide the tasks fairly. The roles were chosen based on the skills of each member, as shown in Figure 4.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Public - علم

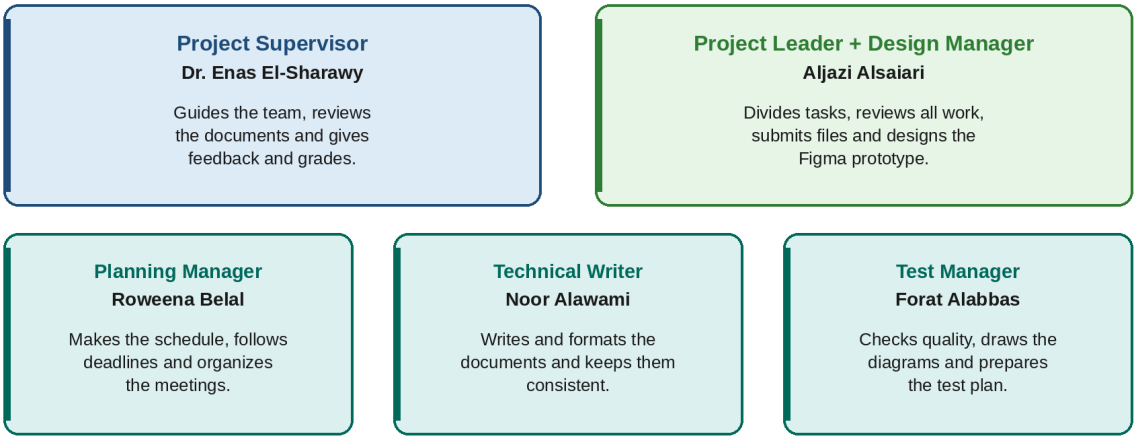


Figure 4: Roles and responsibilities

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

3. Managerial Process Plans

3.1 Start-up Plan

This part explains how we estimated the time of the project, who is working on it, and what training we need to build the Food Saver prototype.

3.1.1 Estimates

This project is part of the software engineering course, so there are no real financial costs. We used an experience-based estimation technique [11], where the estimate is based on the course schedule on Blackboard and our experience in previous course projects. We did not use an algorithmic model such as COCOMO [11], because it estimates the effort based on the size of the code in thousands of lines (KLOC). Our project is a Figma prototype without coding, so there is no code size to measure, and the experience-based estimate is more suitable for us. We re-estimate it after each sprint.

Estimated duration per activity:

- Defining the project (idea, proposal, and SPMP): 7 weeks.
- Detailed documentation (SRS, SDS, STP, and status reports): 6 weeks.
- Prototype improvement and final presentation: 2 weeks.

Total duration of activities: 15 weeks.

3.1.2 Staffing

Our team has four students who chose to work together:

- **Aljazi Alsaiari:** Project Leader and Design Manager; divides the tasks, reviews our work and designs the prototype.
- **Roweena Belal:** Planning Manager.
- **Noor Alawami:** Technical Writer.
- **Forat Alabbas:** Test Manager.

3.1.3 Project Staff Training

No official training is needed. All team members are taking the Software Engineering course (CS 411) with Dr. Enas El-Sharawy. Most of the members already know how to use Figma from previous courses, so they can design the prototype without extra training. When needed, members learn from online tutorials, the course slides and advice from the instructor.

3.2 Work Plan

This part shows how the work is divided into tasks, when each task will be done, and what resources and budget are needed.

3.2.1 Work Breakdown Structure

Figure 5 shows the work breakdown structure of the Food Saver project. The work is divided into five main parts: planning, requirements, design, testing, and closeout.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

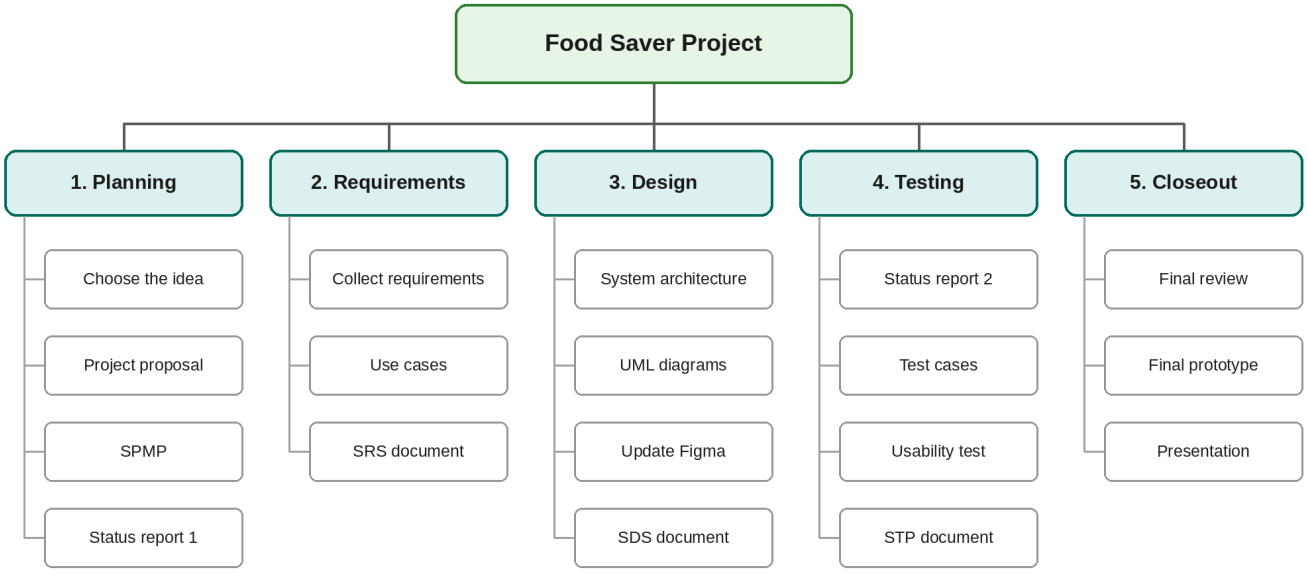


Figure 5: Work breakdown structure

3.2.2 Schedule Allocation

The project timeline follows the official schedule of CS 411. Table 2 divides the work into 12 tasks, based on the planning method in our course book [11]. For each task, it shows the effort in person-days, the duration in working days (5 days per week), and the tasks that must be finished before it starts. The milestones in brackets (M1 to M8) are explained in Table 3. The total effort of all tasks is 60 person-days, which matches the 480 person-hours in section 1.4.2.

Table 2: Project tasks, durations and dependencies

Task	Effort (person-days)	Duration (days)	Dependencies
T1: Choose the idea and survey users	3	10	
T2: Write the project proposal	4	10	T1
T3: Write the SPMP	10	15	T2 (M1)
T4: First status report	2	5	T3 (M2)
T5: Collect requirements and use cases	6	10	T3 (M2)
T6: Write the SRS	5	5	T5
T7: Update the Figma prototype	10	20	T3 (M2)
T8: UML diagrams and write the SDS	6	5	T6 (M4)
T9: Second status report	2	5	T8 (M5)
T10: Usability test with users	3	5	T7
T11: Write the STP	5	5	T8 (M5), T10
T12: Final review and presentation	4	10	T9 (M6), T11 (M7)
Total	**60**	**75 (15 weeks)**	

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Table 3: Project milestones

Milestone	Description	Week
M1	Project proposal approved (end of T2)	Week 4
M2	SPMP submitted (end of T3)	Week 7
M3	First status report submitted (end of T4)	Week 8
M4	SRS submitted (end of T6)	Week 10
M5	SDS submitted (end of T8)	Week 11
M6	Second status report submitted (end of T9)	Week 12
M7	STP submitted (end of T11)	Week 13
M8	Final prototype and presentation (end of T12)	Week 15

Figure 6 shows the activity bar chart of the tasks over the 15 weeks, and Figure 7 shows the staff allocation chart, which explains who works on each task. Some tasks run at the same time, like updating the prototype (T7) while writing the SRS (T5 and T6). The critical path is T1, T2, T3, T7, T10, T11 and T12, so any delay in these tasks will delay the whole project.

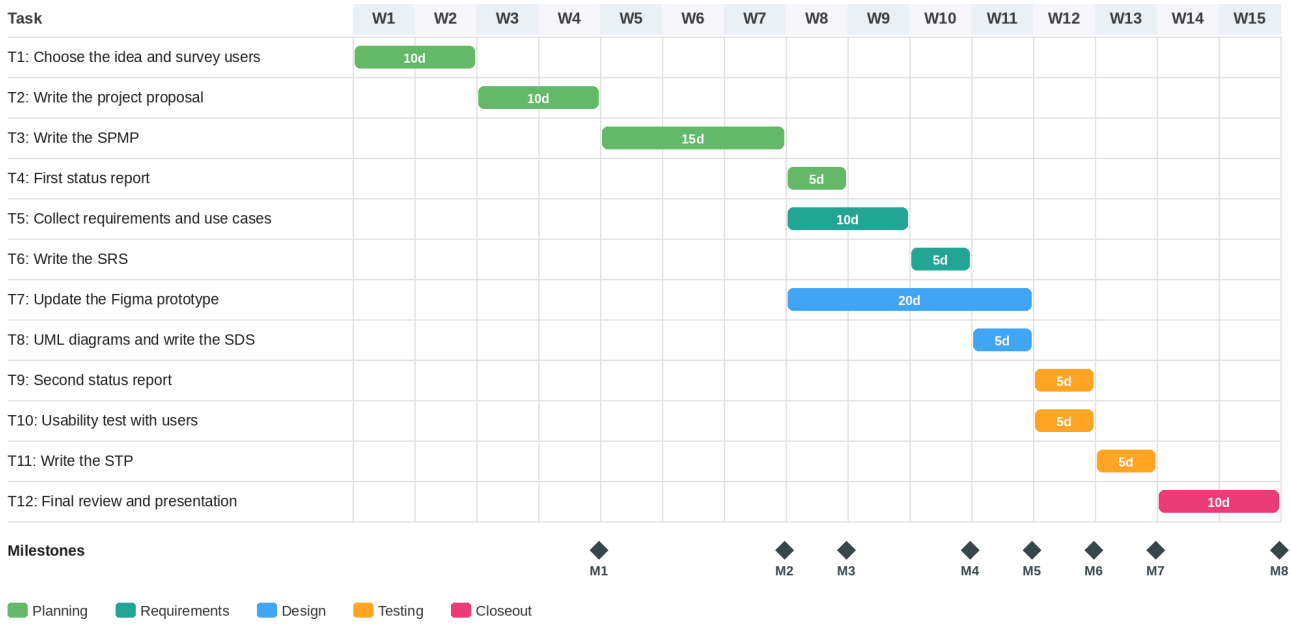


Figure 6: Activity bar chart

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

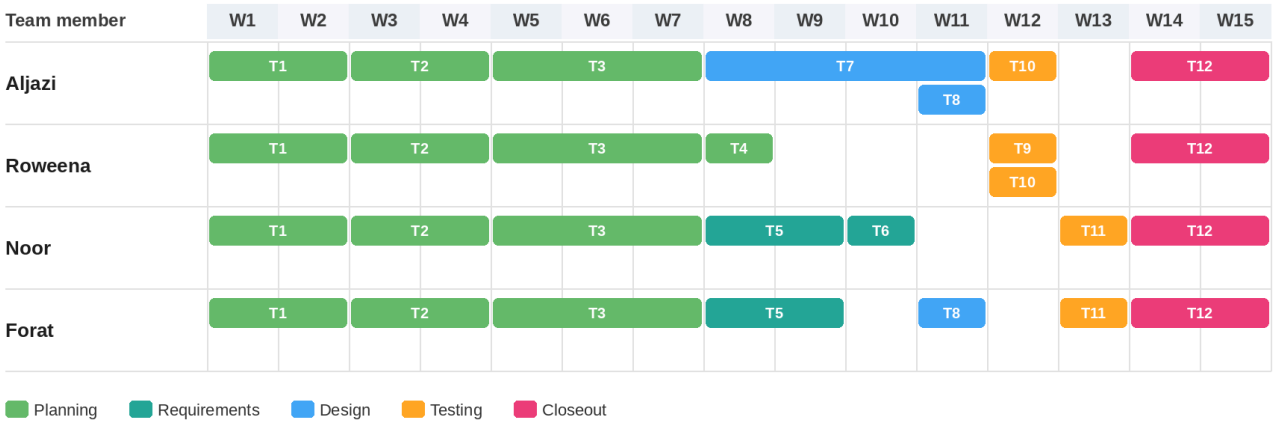


Figure 7: Staff allocation chart

3.2.3 Resource Allocation

All resources in this project are personal or free. Each team member uses her own device to do the tasks. We use Figma to design the prototype, Canva for the figures, and Microsoft Word and Google Docs to write the documents. For communication, the team uses WhatsApp for quick updates and Zoom for online meetings. The team has four students with different skills in design, planning, writing, and testing. No extra resources are needed.

3.2.4 Budget Allocation

No budget is allocated for this project because all main resources are free or owned by the team. The documents are written on personal devices using free or university versions of Microsoft Word, Google Docs, Figma, and Canva. Meetings are held online or at the university, so there is no travel cost.

Total personal expenses: about 600 SAR (see section 1.4.2).

3.3 Project Tracking Plan

This part explains how we follow the progress, control changes, and keep the quality of the documents and the prototype.

3.3.1 Requirements Management

Requirements are collected through team discussions, a short survey with possible users, and feedback from the instructor. The prototype also helps by checking the requirements early, due to the fact that the members can view and click the screens before the end of the SRS. Any change in the requirements is discussed in the team meeting first to see how it affects the scope, schedule, and documents. After the team agrees, the change is written in the shared files, and all members are informed. The team leader makes sure that each requirement is connected to its design in the SDS and its test in the STP.

3.3.2 Schedule Control

The team checks the progress every week and compares it with the course schedule. If a task is late, the task is given to another member or we hold an extra meeting to finish it. The members use

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

WhatsApp updates and the Sprint Backlog to follow the status of each task. Before any submission, the team leader checks that the document is complete.

3.3.4 Quality Control

Every document is reviewed by at least one other member before submission to make sure it is complete and correct. Grammar, formatting, and consistency between the documents are checked. After that, the team leader does the final review. All documents follow the IEEE standards and the course template. The members also use the instructor feedback to improve the next versions.

3.3.5 Reporting

WhatsApp is used for quick updates and questions and Zoom for online meetings when needed. The team also meets before each submission deadline. After each meeting, a short summary is shared with all members in the WhatsApp group. The progress is also discussed with the instructor during class or office hours when needed.

3.3.6 Project Metrics

The project progress is measured using simple metrics:

Table 4: Project metrics

Metrics	Frequency	Reporting Process
Document completion percentage	Weekly	Reviewed by the ScrumMaster
On-time submission rate	Per deliverable	Compared with the course deadlines
Team participation	Weekly	Checked in team meetings
Quality review results	Per deliverable	Reviewed by team members
Instructor feedback	Per submission	Recorded in team notes

3.4 Risk Management Plan

The Food Saver team follows a simple risk management process with four steps: identifying the risks, analyzing them, planning how to deal with them, and monitoring them during the project [11]. The members discuss the risks in meetings and try to solve problems before they cause delays.

The three tables below show the main risks, their probability and effects, and the plan to reduce them. In Table 6, each risk is also given a risk level (High, Medium or Low) based on its probability and consequences, so the team can focus on the most dangerous risks first.

Table 5: Risk identification

Risk Identification	Affects	Type
R1: Time constraints because of underestimating the work	Project and product	Estimation
R2: A member is absent at a critical time	Project	People
R3: Losing files because of device or internet problems	Project and product	Technology
R4: Too many features for one semester	Product	Requirements
R5: Weak academic writing	Product	People
R6: Prototype design problems	Product	Technology

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

Risk Identification	Affects	Type
R7: Disagreements between team members	Project and product	Organizational

Table 6: Risk analysis

Identified Risk	Probability	Consequences	Risk Level
R1	High	Serious	**High**
R2	Moderate	Serious	**Medium**
R3	Moderate	Serious	**Medium**
R4	High	Tolerable	**Medium**
R5	Moderate	Tolerable	**Low**
R6	Moderate	Tolerable	**Low**
R7	Moderate	Tolerable	**Low**

Table 7: Risk planning

Identified Risk	Strategy
R1	Follow a clear schedule, divide the tasks early and avoid last-minute work.
R2	Each member should understand the work of the others so anyone can continue.
R3	Save the work regularly and keep all files on Google Drive.
R4	Focus on the main features first (inventory, alerts, recipes and donation).
R5	Review the documents together and use writing tools before submitting.
R6	Test the prototype with users early and fix the problems in the next version.
R7	Solve disagreements by discussion or voting to reach a fair decision.

The team will keep checking these risks during the project and update the plan if new problems appear.

3.5 Project Closeout Plan

At the end of the Food Saver project, the team will close the project in an orderly manner:

1. **Final Review:** Each member reviews their section and verifies that all project goals have been achieved.
2. **Final Presentation:** the team prepares the final prototype and presentation that summarizes the project, the challenges we faced and the lessons learned.
3. **Project Closure:** The project is considered complete when all documents and presentation are submitted and approved.

All final files will be saved in a Google Drive folder.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

4. Technical Process Plans

This section describes the process model, tools and the environment used to create the Food Saver prototype, write the accompanying documentation, and how the work will be accepted.

4.1 Process Model

The Food Saver project makes use of an adaptation of the Agile Scrum methodology [12]. The project is broken up into short work sprints that each end with either a document or a revised version of the prototype. After each sprint, the team meets to review the work and make changes based on the feedback from the instructor.

In Scrum, there are three main roles [11]. There is no real client for our project, so the project leader (Aljazi) is the product owner. She speaks for the end users and determines which features get priority, based on survey results. Roweena is the planning manager and plays the role of ScrumMaster. She organizes the meetings, follows the backlog, and checks our progress. All four of us are the development team. Our main stakeholder is the instructor who looks at our work when we submit it.

We have a Product Backlog. This is just a list of everything we have to do, the eight modules of the prototype and the documents we have to produce. At the beginning of each sprint we select items from this list and they become the sprint backlog for that sprint. We cannot meet face to face on a daily basis, so we use a distributed Scrum style [11]. For our daily scrum we just do a quick update in the WhatsApp group and if we need a longer discussion we meet on Zoom.

The first project document, the SPMP, will define the project management plans including the start-up, work, tracking, risk and closeout plans, as well as the technical and supporting plans after the project idea and proposal are approved in week 4. This will be done by the end of week 7.

In week 8 a first status report will be written to show how the project is progressing. The second document, Software Requirements Specification (SRS), will be prepared in week 10. It will describe who the users are and what Food Saver does. The third document, the Software Design Specification (SDS), will be created in week 11 and will describe the system design, screens and diagrams. The second status report will be produced in week 12. The last document, the Software Test Plan (STP) will be produced in week 13, describing the test cases and acceptance criteria.

Each document will be reviewed by the team before it is submitted, and the feedback from the instructor will be used to improve the next document. Some work can also be done in parallel, e.g. the prototype development and SRS writing as shown in Table 2. The final Figma prototype will be delivered at the end of week 15, and the project will be presented in the same week.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

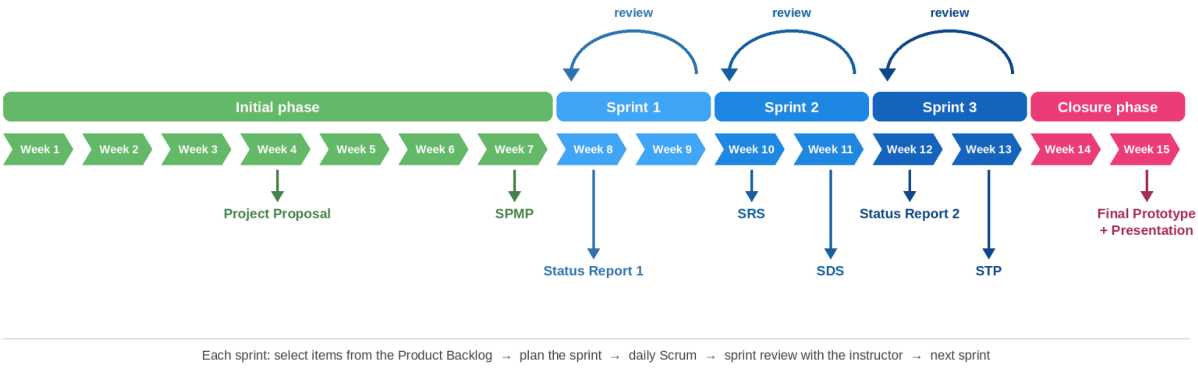


Figure 8: Scrum process model of the project

4.2 Methods, Tools, and Techniques

The project follows the Agile Scrum method, and each sprint ends with a review of its work, which can be a document or an updated version of the prototype. For example, Sprint 1 ends with a review of the collected requirements and the first prototype update. If something needs to change, the team fixes it in the next sprint.

The team will split up the sections of each document evenly before they start. As each member writes their section, the leader will review the entire document and send back errors to the member responsible. The documents are written in Microsoft Word and Google Docs, and the figures are designed in Canva. The prototypes are created in Figma, which allows our team members to create interactive screens without coding, and they already have experience using Figma. Documents respect the IEEE standards and the course templates. Every version of a document is saved with a meaningful name in the shared Google Drive folder; the final documents are submitted in the Blackboard.

4.3 Infrastructure

The team members use their personal devices with internet access for searching, communication, and submitting the work. The main software we use is Microsoft Word, Google Docs, Figma, Canva, Zoom, and WhatsApp. No special physical place is needed, and the team follows the university rules for data and file security.

4.4 Product Acceptance

The instructor reviews each document after the team leader submits it, then gives feedback and a grade based on the rubric on Blackboard. The rubric works as our acceptance criteria. The main criteria are clarity, organization, following the IEEE template, complete content, and references. If the work is not accepted, the team will prepare a new version until it is approved.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

5. Supporting Process Plans

5.1 Documentation

The project documents follow the university templates and the IEEE standards: IEEE 1058 for the SPMP [9], IEEE 830 for the SRS [13], IEEE 1016 for the SDS [14], and IEEE 829 for the STP [10]. All files are saved in a shared Google Drive folder so every member can access them. Before each submission, the documents are reviewed to make sure they are complete, correct, and match the project goals. The team also meets every week to follow the progress and make sure all documents are consistent.

Table 8: Details about project documents

Document	Deadline	Template	Prepared By	Review Before Submitting
Project Proposal	Week 4	University Template	All Team Members	The Leader
SPMP	Week 7	IEEE 1058	All Team Members	The Leader
Status Report 1	Week 8	Course Template	All Team Members	The Leader
SRS	Week 10	IEEE 830	All Team Members	The Leader
SDS	Week 11	IEEE 1016	All Team Members	The Leader
Status Report 2	Week 12	Course Template	All Team Members	The Leader
STP	Week 13	IEEE 829	All Team Members	The Leader
Final Prototype and Presentation	Week 15	Course Template	All Team Members	The Leader

Copyright © 2026 by CS Year 5 – SE Old Section – G1.

6. Additional Plans

We also have a few additional plans to keep the project organized: a plan to update the project documents, a plan to review and improve the written work, and a plan for privacy and security. The app needs the location of its users, so the prototype will only use sample data. In a real version, the exact address of a donor would only be shown after a donation is accepted. We will also collect feedback from the test users and write it down as ideas for the future, such as adding other languages or working with local food charities. These plans help keep Food Saver consistent and ready to grow in the future.

Copyright © 2026 by CS Year 5 – SE Old Section – G1.
